



# Fire Station 50

**Project Status Update - Monthly Report**  
March 2022



## PROJECT STATUS:

- **Time:**
  - Project completion date was extended 42 days due Annex Mold Mitigation
- **Budget**
  - Change order balance -\$45,735.41 (savings)
  - No current contingency authorization requests

## PROJECT PROGRESS:

- Demolition of Existing Fire Station 50 – Complete
- Foundation and structural work are currently underway, including the following:
  - Concrete / steel columns – Complete
  - Fill & soil termite treatment – Complete
  - Underground plumbing – Complete
  - Underground electrical – Complete
  - Reinforcing and pouring slab – Complete
  - Putting up CMU walls – Starting 3/31/22


## CHANGE ORDERS:

#	Description	Date Created	Type	Dollar Amount	Sales Tax Savings
1	Doors and Hardware - DMP	12/06/21	Deduct	-\$200,130.30	\$11,375.00
2	Plumbing Trim Materials - DMP	12/07/21	Deduct	-\$78,157.94	\$4,471.20
3	Lighting Fixtures - DMP	12/07/21	Deduct	-\$138,768.81	\$7,902.01
4	Lamp Metal Trusses - DMP	12/07/21	Deduct	-\$103,930.00	\$5,930.00
5	Metal Roof Decking Materials - DMP	12/07/21	Deduct	-\$65,770.00	\$3,770.00
6	Generator & Transfer Switch - DMP	12/08/21	Deduct	-\$158,859.20	\$9,039.20
7	Time Extension - 42 Days (Annex IAQ Remediation)	12/15/21	Time	\$0.00	\$0.00
8	Fabricated Rebar - DMP	12/17/21	Deduct	-\$56,548.00	\$3,248.00
				-\$802,164.25	\$45,735.41

### DMP = Direct Material Purchases

- Direct material purchases have been implemented into this project to capitalize on the sales tax saving
- Current DMP savings for Fire Station 50 are \$45,735.41
- Two (2) previously listed DMPs were canceled due to conflicts with the project's grant funding

# PROJECT SCHEDULE:

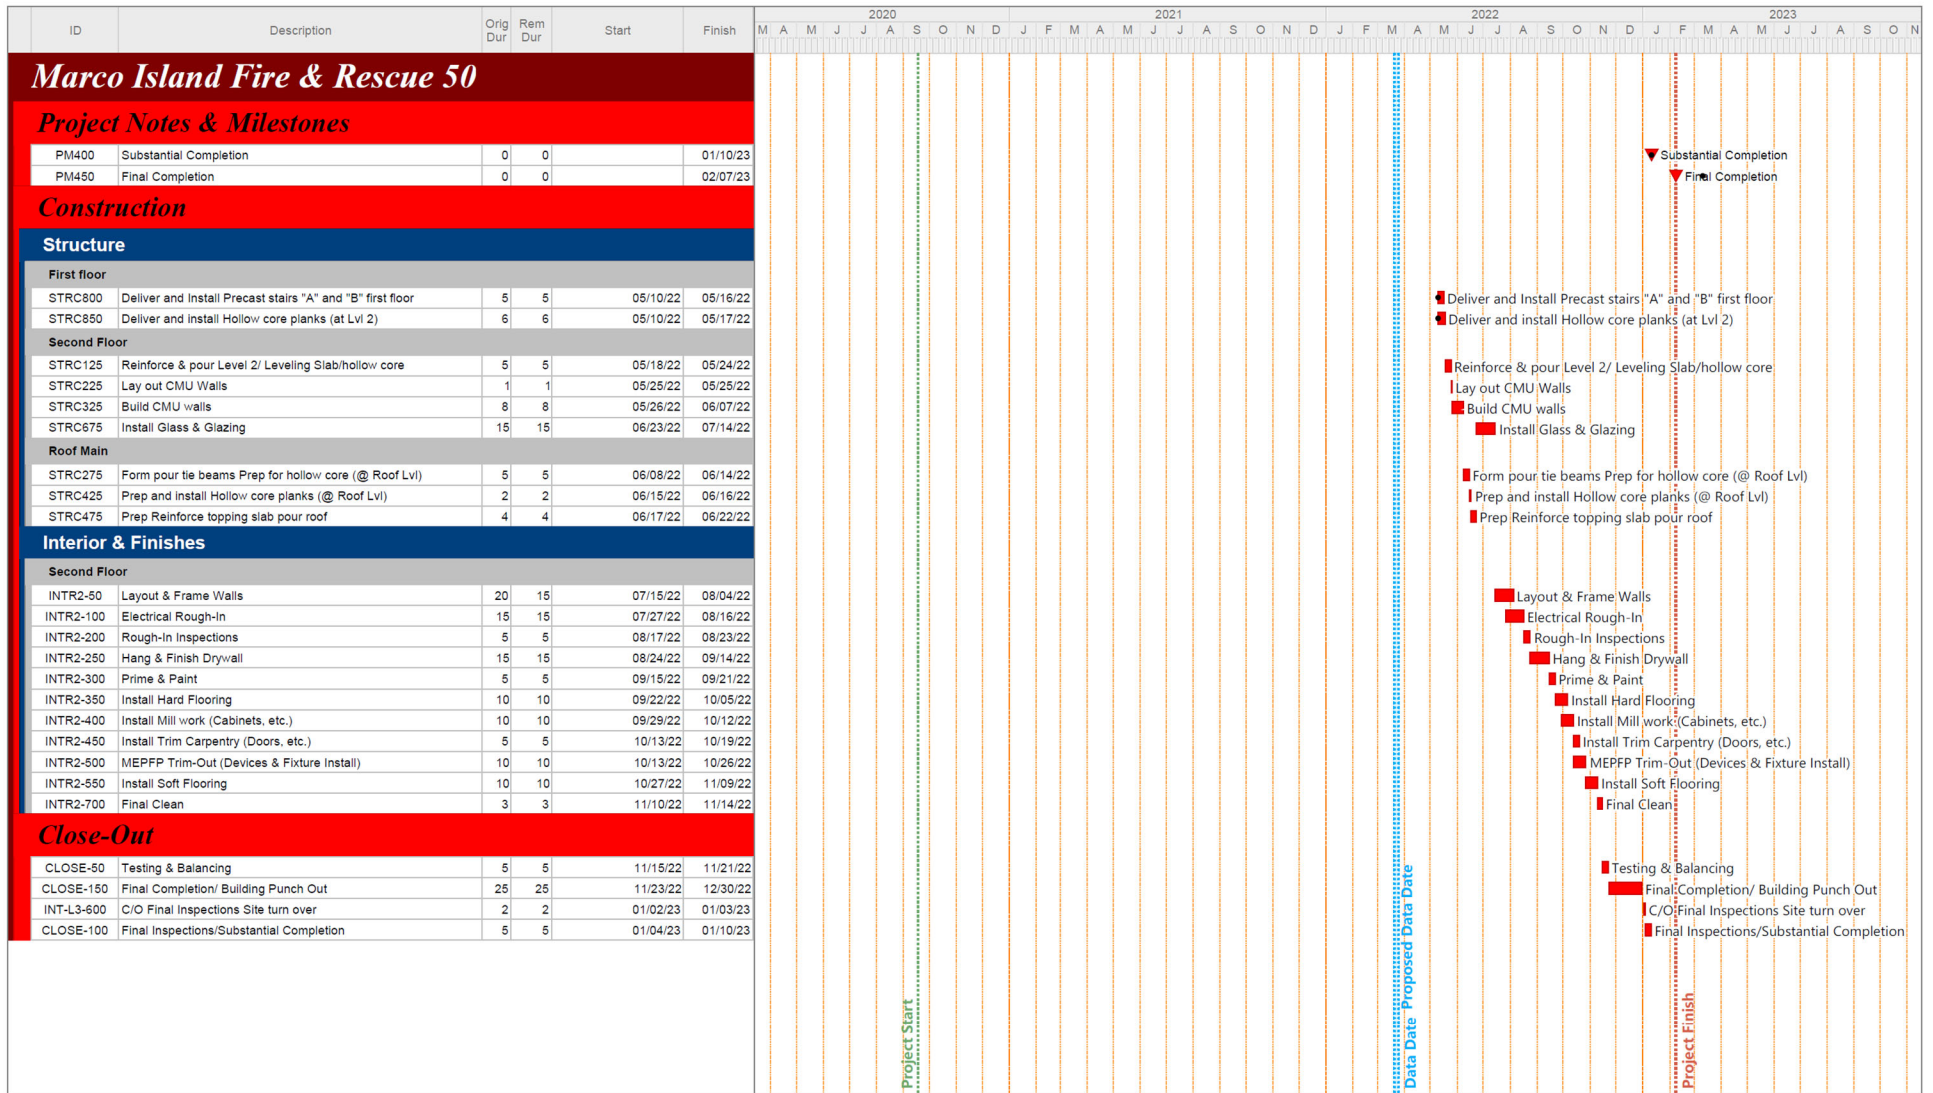

Start Date: 09/18/20  
 Finish Date: 02/08/23  
 Data Date: 03/25/22  
 Run Date: 03/25/22  
 4027-MF08.ppx

**CITY OF MARCO ISLAND**  
**FIRE & RESCUE STATION 50/EOC**  
**MCC PROJECT # 4027**



Exhibit A:



November 2021



December 2021



January 2022



727.520.8181  
www.aerophoto.com

Marco Island Fire Rescue Station 50

Image # 22  
Date 03.03.22

February 2022



*Fire Station 50 – Underground Plumbing*



*Fire Station 50 – Underground Electrical and Plumbing*



*Fire Station 50 – Underground Electrical and Plumbing*



*Fire Station 50 – Concrete Slab Prep*



*Fire Station 50 – Concrete Slab Pour*



*Fire Station 50 – Concrete Slab*



*Fire Station 50 – Concrete Slab*



*Fire Station 50 – Setup for CMU Walls*
